
Stages and costs

The Volvac brand, website and marketing, from the concept you have seen to a live site that buyers can find. What happens at each stage, what each stage costs, and why.

Prepared for Volvac by SocialHat, 13 October 2026.

Stills throughout are taken from the concept homepage. Readings shown on instruments are illustrative.

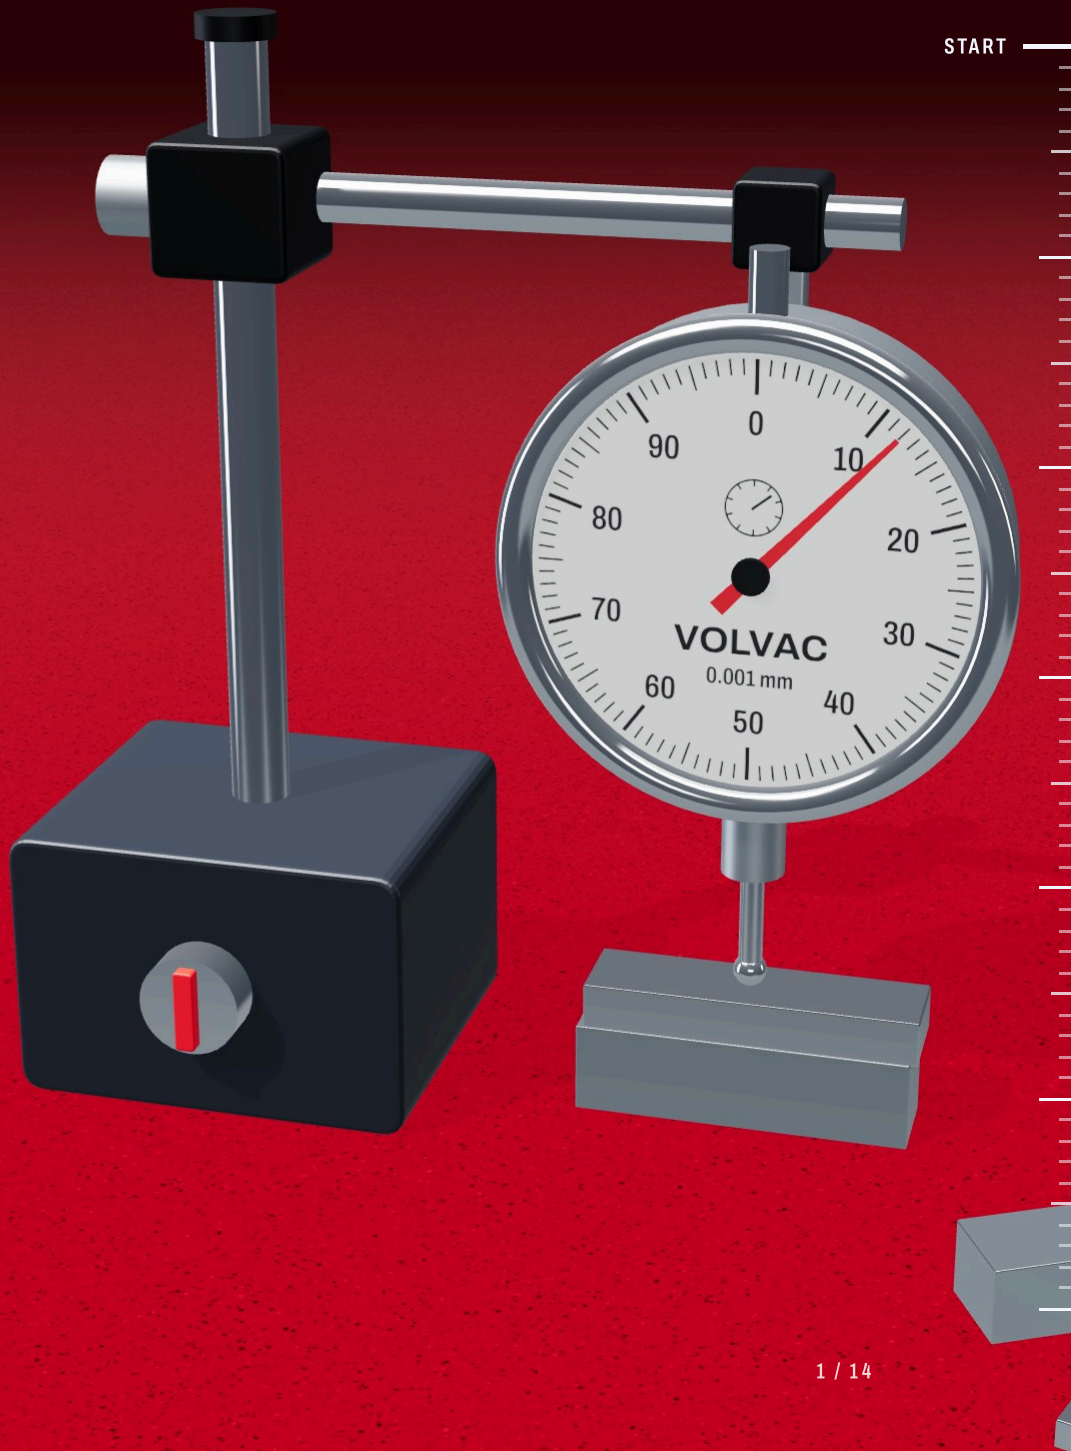

Three months, two tracks.


The concept is finished and cost you nothing. From here the website runs in three stages, one a month, at A$2,000 each. Marketing runs beside it, also one stage a month, and is included in that price, so that buyers are already following Volvac on the day the site goes live. Each stage closes with something you can see and sign off, and the next is not started until you have approved it.

WEBSITE, THREE STAGES
A$6,000

MARKETING, THREE STAGES
Included

INVOICED MONTHLY
3 × A$2,000

CONCEPT TO LIVE SITE
3 months

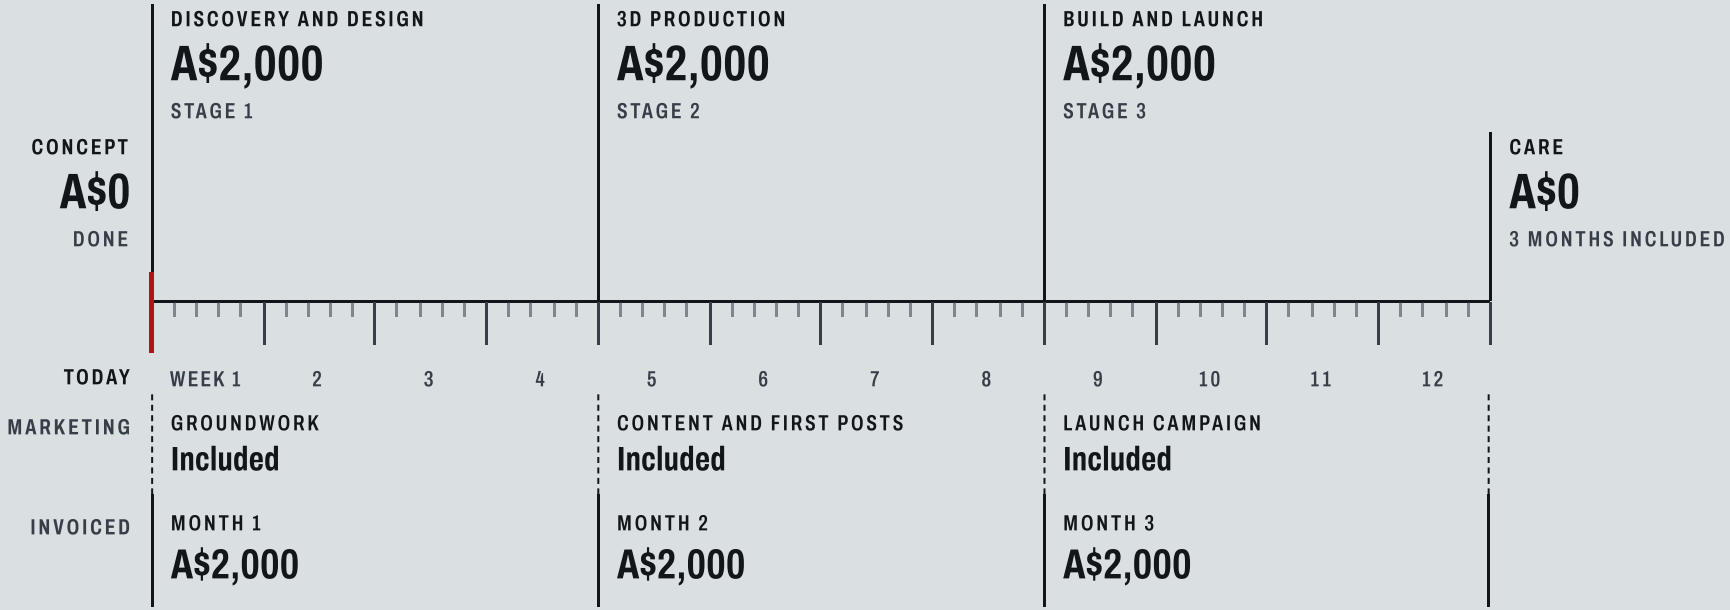

Why it is staged, and why in this order.

Decisions come before production.

Facts, structure and identity are settled first because every later stage is built on them. Changing a wordmark before the 3D is finished is a small job. Changing it afterwards is a large one.

Each price is a count, not a guess.

One homepage journey, ten maker pages, six services, two contact lines. The scope can be counted, so each stage can be fixed. If a stage runs long, that is our cost and not yours.

The largest stage is already proven.

3D production takes the most skilled hours and is what sets the site apart. The concept already models all six instrument groups and runs in a browser, so that stage finishes existing work instead of starting from nothing.

Three equal invoices.

Each month is one invoice of A$2,000, covering the website stage and the marketing stage beside it, so the cost arrives evenly. Each stage ends on a sign-off, so you are never committed further than the month you are in.

Stage 0: the concept, already delivered.

Before asking for a decision we built the part that is usually argued about longest: what the brand looks like, and whether the idea works. You have now seen both.

STATUS
Complete

COST TO YOU
A$0


WHAT EXISTS	A new wordmark, colour system and single typeface. A homepage in real 3D: one granite inspection plate carrying six instrument groups, each modelled in code and animated. Ten makers and six services laid out with wording drawn from your current site. Nine social posts, each in portrait and landscape, and three sample posts in Volvac's current brand.
WHY NO CHARGE	The creative direction is our risk to take. It also means every price that follows is for building something you have already seen, not for exploring.




LEAK, FLOW AND PRESSURE



REFRIGERATION



MARKING



BALANCING



PACKAGING




Stage 1: discovery and design

STAGE 1

RUNS	STAGE COST	INVOICED
Weeks 1 to 4	A$2,000	Month 1

WHAT HAPPENS	One working session with you, then we confirm the facts we could not verify from outside and settle the final wordmark and colours. Every page is then designed and written before anything is built, for desktop and phone, from your existing material and your corrections.
YOU RECEIVE	An agreed sitemap, final logo files and a short brand guide, and the whole site as a clickable outline you can read page by page, with final wording.
WHY THIS COST	Decisions come first because they are cheapest to change here. The cost is the number of distinct layouts and the writing. Pages that share a template are designed once.
YOU SIGN OFF	The identity, the page designs and the wording.

From the concept: dot peen marking station

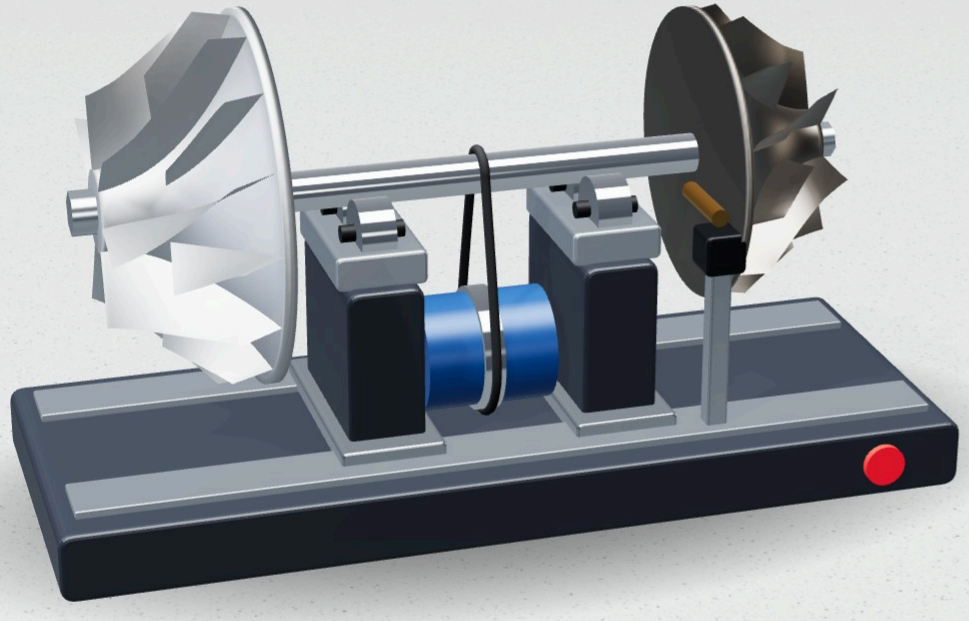

From the concept: turbocharger rotor on the balancer

Stage 2: 3D production

RUNS	STAGE COST	INVOICED
Weeks 5 to 8	A$2,000	Month 2

WHAT HAPPENS	The instrument groups from the concept are taken to production standard. Each model is checked against the real product it stands for and corrected where the concept took liberties. Animations are tuned, the page is made to run smoothly on an ordinary office laptop and a mid-range phone, and a still version is built for devices that cannot run 3D.
YOU RECEIVE	The finished 3D scene, running in a browser, to review on your own devices.
WHY THIS COST	It is the most skilled work and the part no template can supply. It would be larger if the concept had not already modelled every instrument and proved the approach. What is left is accuracy, finish and speed.
YOU SIGN OFF	The models and the motion.



From the concept: chamber vacuum packer

Stage 3: build and launch

RUNS	STAGE COST	INVOICED
Weeks 9 to 12	A$2,000	Month 3


WHAT HAPPENS	The approved designs become the working site, with enquiries routed to sales or to technical support and search setup in place. It is tested on phones, tablets and laptops, every address on the current site is redirected so existing links keep working, and the site goes live on your domain. We finish with a handover session for your team.
YOU RECEIVE	The live site, the redirect map, and handover notes.
WHY THIS COST	Countable parts: the pages built from the approved designs, search setup, the test matrix and the redirect map from the old site.
YOU SIGN OFF	The complete site before it goes public, then go live.

Marketing, made by the people who made the brand.

A new site pays for itself when buyers find it. Our own team of graphic designers makes Volvac's posts from the same 3D models as the site. We write them and post them, and we look after search, so that buyers in your export markets find Volvac when they look for a machine.

SOCIAL MEDIA	A content plan, designed posts and short 3D clips for Instagram, LinkedIn, Facebook and YouTube, written, scheduled and posted for you. Comments answered, and enquiries passed to your team.
SEARCH	Keyword research for the markets you sell to most, page titles and descriptions, product markup, Google Search Console and your Google Business Profile, then articles that answer what buyers search for.
REPORTING	One page a month: reach, followers, search rankings, and the enquiries that came from each.







Three sample posts made for this proposal, in Volvac's current brand and from the concept's 3D models. All three are in samples.html, in portrait and landscape.

Marketing stages, one a month beside the site

Each marketing stage runs in the same month as a website stage, uses what that stage produces, and ends on its own sign-off. All three are included in the monthly A$2,000, at no extra cost.

MARKETING 1

Groundwork

RUNS	BESIDE	COST
Month 1	Stage 1	Included

WHAT HAPPENS

We audit your current Instagram, LinkedIn, Facebook and YouTube accounts and where Volvac stands in search today. We research the words buyers use for your machines in the markets you sell to most, and agree what to post, how often, and in what voice.

YOU RECEIVE

A content plan and posting calendar, and a keyword map that sets the page titles and wording of the new site before it is built.

YOU SIGN OFF

The plan and the keyword map.

MARKETING 2

Content and first posts

RUNS	BESIDE	COST
Month 2	Stage 2	Included

WHAT HAPPENS

Our designers turn the signed-off identity into post templates for every channel and format. Posting starts: twelve posts across the month, made from the 3D models and your product range, so an audience is building before the site launches.

YOU RECEIVE

The template set, twelve published posts, and the first month's numbers.

YOU SIGN OFF

The templates, and each week's posts before they go out.

MARKETING 3

Launch campaign

RUNS	BESIDE	COST
Month 3	Stage 3	Included

WHAT HAPPENS

Teaser posts in the run-up, then launch day across every channel with short clips from the 3D scene. On the site, every page gets its search title, description and product markup, the sitemap goes to Google, and Search Console, analytics and your Google Business Profile are set up.

YOU RECEIVE

The launch campaign, a site search engines can read from its first day, and a baseline report to measure from.

YOU SIGN OFF

The campaign before it goes out.

Three months of care included

A website runs on browsers, phones and search engines that keep changing, and someone should own that. Standard Care is included for the first three months. After that, care is optional and monthly.

Lite Care **A$150 a month**	Hosting checks, uptime monitoring, and small fixes.
Standard Care **A$350 a month** FIRST THREE MONTHS INCLUDED	Everything in Lite, plus regular updates and security patches, support from a real person, and minor changes to text and images on request.
Full Care **A$650 a month**	Everything in Standard, plus priority support, ongoing feature work, and performance reporting.

Three months of Standard Care is worth A$1,050. A new site collects small requests in its first months, and this covers them without a quote each time.



AFTER LAUNCH

From the concept: manifold gauge set and charging cylinder

Marketing after launch, month by month

From month four, marketing carries on as a monthly plan. You can move between plans or stop with a month's notice. We recommend Social and Search for the first year, while the site builds its place in search.

Social
A$650 a month

Twelve designed posts a month across Instagram, LinkedIn and Facebook, written, scheduled and posted for you. Comments answered, and enquiries passed to your team. A one-page report each month.


Social and Search
A$1,200 a month
RECOMMENDED

Everything in Social, plus four short clips a month made from the 3D models, one article or product page a month written for search, ongoing search fixes across the site, and rankings and enquiries in the monthly report.

Growth
A$2,100 a month

Everything in Social and Search, plus twenty posts a month, YouTube, and paid campaigns on LinkedIn and Meta set up and run for you. Ad spend is paid to the platforms directly.

Every plan includes the design work: posts are made by our designers in the Volvac identity, not from stock templates.

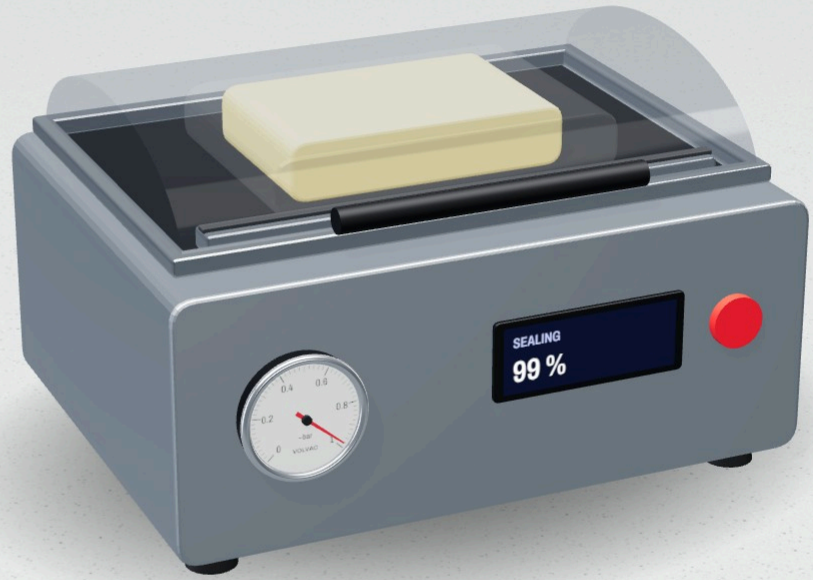

From the concept: chamber vacuum packer

Options you can add at any sign-off

None of these is needed to launch. Each has a flat price and can be added at a sign-off or after the site is live.

AI assistant
A$900

Answers product questions from your own pages at any hour, and passes the enquiry to sales or technical support with the details attached.

Augmented reality
A$1,500

Lets a buyer place a machine at true size on their own floor through a phone camera, before they call.

Data and analytics
A$800

A dashboard showing which makers and pages bring enquiries.

Extra pages
A$200 each

For example, one page for each of the eight industries you serve.



From the concept: one engraved gauge block for each maker

How the three months add up

Three invoices of A$2,000, each issued when its month begins. Each invoice pays for one website stage, and the marketing stage beside it is included.

INVOICE	STAGE 1 Discovery and design	STAGE 2 3D production	STAGE 3 Build and launch	INVOICE TOTAL
Month 1 Weeks 1 to 4, issued at the start	A$2,000	0	0	**A$2,000**
Month 2 Weeks 5 to 8, issued at the start	0	A$2,000	0	**A$2,000**
Month 3 Weeks 9 to 12, issued at the start	0	0	A$2,000	**A$2,000**
Stage cost	**A$2,000**	**A$2,000**	**A$2,000**	**A$6,000**

- Prices are in Australian dollars and exclude any taxes that may apply.
- Each month is invoiced when it begins. The next month starts only after sign-off.
- Timings assume feedback within two working days at each sign-off.
- Marketing stages 1 to 3 are included in the monthly price and are not invoiced separately.
- From month four, the marketing plan you choose is invoiced monthly and can be changed or stopped with a month's notice.
- Standard Care is included for three months from launch. After that, care is optional.
- Not included: photography or filmed video, advertising spend, and fees charged by third parties such as domain registration and hosting.

The next step is stage 1.

A$2,000 and four weeks, with marketing included. It ends with the whole site decided on paper: the sitemap, the finished identity, every page designed and written, and the marketing plan and keyword map agreed. Once that is signed off, the site is two months from live.

To approve stage 1, or to ask anything

info@socialhat.com.au

Website

socialhat.com.au

